



EXECUTIVE OVERVIEW

RISK INTELLIGENCE

RISK ID

▼

DISTRICT

▼

TYPE

▼

STATUS

▼

SEVERITY

▼

All

▼

All

▼

All

▼

All

▼

All

▼

Executive Overview

Risk Exposure

Heatmap

Treatment Tracker

Milestone Impact

Risk Deep Drive

Risk Details

TOTAL RISKS

130

OPEN RISKS

32

HIGH RISKS (≥15)

11

CLOSED RISKS

97


RISKS REDUCTION %

68%


AVG. INHERENT

10


RISK STATUS BREAKDOWN

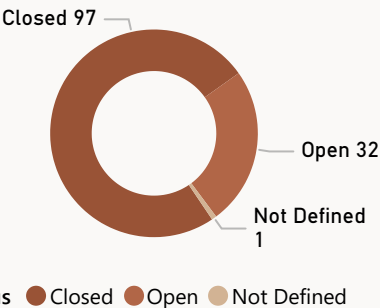

RISK TYPE DISTRIBUTION

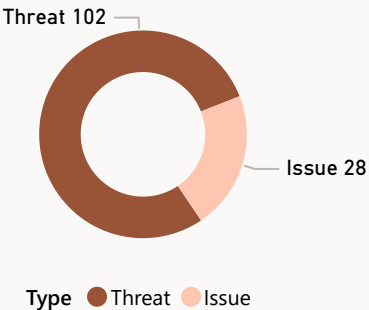

TREATMENT STRATEGY MIX

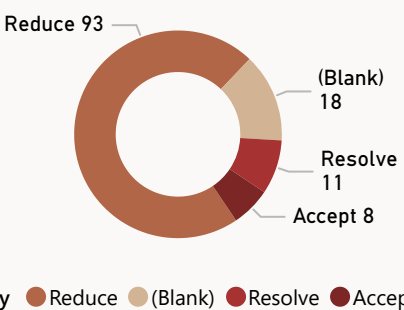

TOP 5 OPEN RISKS BY INHERENT SCORE

RTH743

Risk ID

TBI

District

20

Inherent Risk Rating

Delay in appoint...

Risk / Issue Title

RTH800

Risk ID

TBI

District

20

Inherent Risk Rating

Potential Change...

Risk / Issue Title

RTH71

Risk ID

TBI

District

16

Inherent Risk Rating

Delayed peer rev...

Risk / Issue Title

RTH832

Risk ID

TBI

District

16

Inherent Risk Rating

Enhancement of ...

Risk / Issue Title

RTH833

Risk ID

TBI

District

16

Inherent Risk Rating

Potential Change...

Risk / Issue Title


AVG. TARGET

3.13

AVG. AGING (OPEN)

175d

SEVERITY DISTRIBUTION

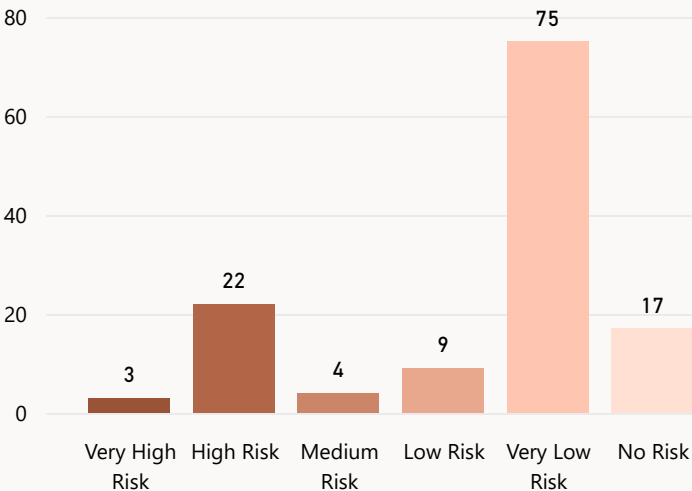

RISKS BY PROJECT





RISK EXPOSURE OVERVIEW

RISK INTELLIGENCE

RISK ID

All

DISTRICT

All

TYPES

All


STATUS

All

SEVERITY

All

- Executive Overview
- Risk Exposure
- Heatmap
- Treatment Tracker
- Milestone Impact
- Risk Deep Drive
- Risk Details

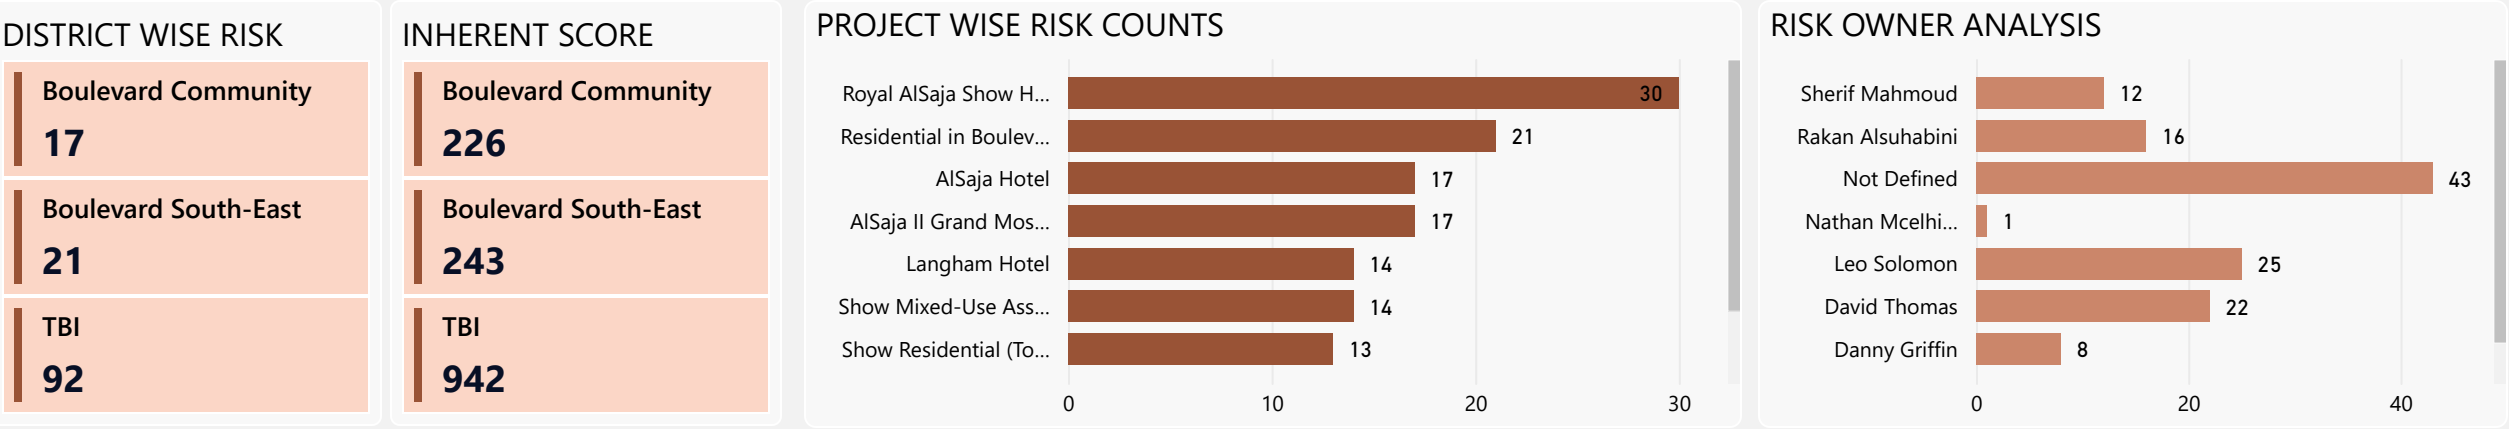

PROJECT :

All

OWNER :

All

RISK EXPOSURE REGISTER									
RISK ID	PROJECT	DISTRICT	OWNER	TYPE	STATUS	INHERENT RISK SCORE	TARGET RISK SCORE	RISK DEDUCTION%	AGING
RTH85	Royal AlSaja Show House	TBI	Leo Solomon	Threat	Closed	12	1	92%	611
RTH842	Langham Hotel	Boulevard Community	Not Defined	Threat	Not Defined	20	20	0%	135
RTH84	Royal AlSaja Show House	TBI	Leo Solomon	Threat	Closed	12	1	92%	611
RTH833	Show Mixed-Use Assets	TBI	Not Defined	Threat	Open	16	16	0%	141
RTH832	Show Mixed-Use Assets	TBI	Not Defined	Threat	Open	16	16	0%	141
RTH83	Royal AlSaja Show House	TBI	Leo Solomon	Threat	Closed	12	1	92%	611
RTH825	AlSaja Residences	TBI	Not Defined	Threat	Open	0	0	0%	193
RTH824	Langham Hotel	Boulevard Community	Not Defined	Issue	Closed	15	0	100%	165
RTH821	Langham Hotel	Boulevard Community	David Thomas	Threat	Closed	0	0	0%	165
RTH820	Langham Hotel	Boulevard Community	David Thomas	Threat	Closed	0	0	0%	165
RTH82	Royal AlSaja Show House	TBI	Leo Solomon	Threat	Closed	16	1	94%	611
RTH818	AlSaja Hotel	TBI	Not Defined	Threat	Closed	0	0	0%	165
RTH817	AlSaja Hotel	TBI	Not Defined	Threat	Closed	0	0	0%	165
RTH816	AlSaja Hotel	TBI	Not Defined	Threat	Closed	0	0	0%	165
RTH815	AlSaja Hotel	TBI	Not Defined	Threat	Closed	0	0	0%	165
RTH81	Royal AlSaja Show House	TBI	Leo Solomon	Threat	Closed	16	1	94%	611
RTH805	Show Residential (Townhouses)	TBI	Not Defined	Threat	Open	0	0	0%	170



RISK HEATMAP OVERVIEW

RISK INTELLIGENCE

RISK ID

All

PROJECT

All

TYPES

All

STATUS

All

SEVERITY

All

Executive Overview

Risk Exposure

Heatmap

Treatment Tracker





Milestone Impact

Risk Deep Drive

Risk Details

INHERENT

TARGET

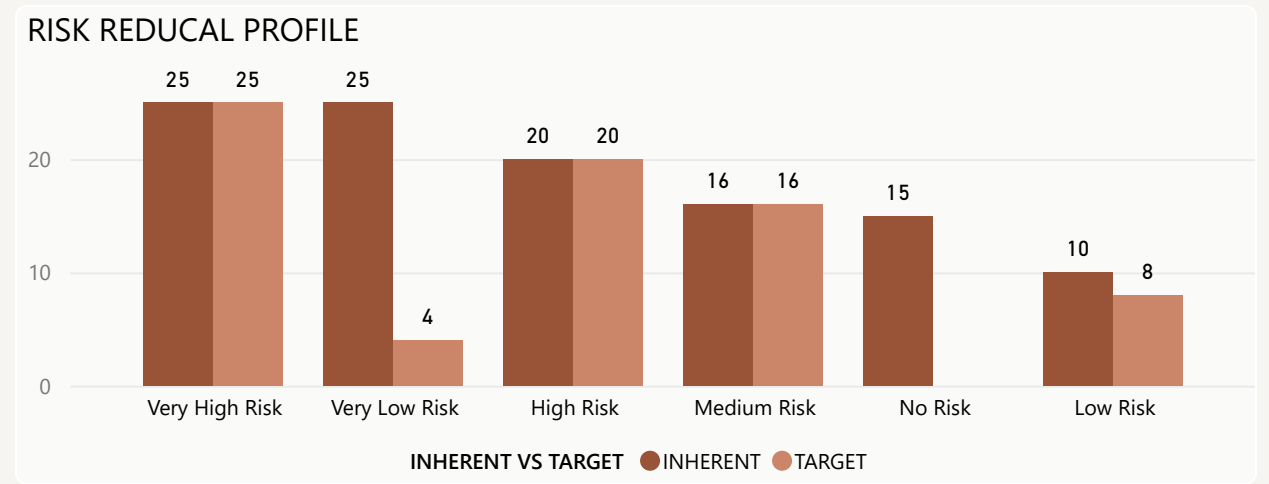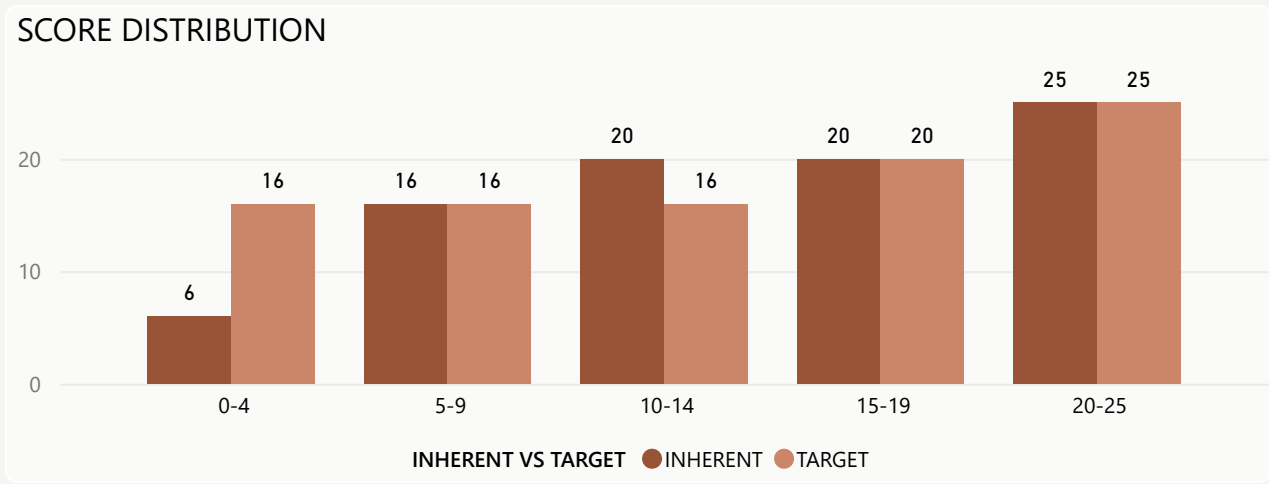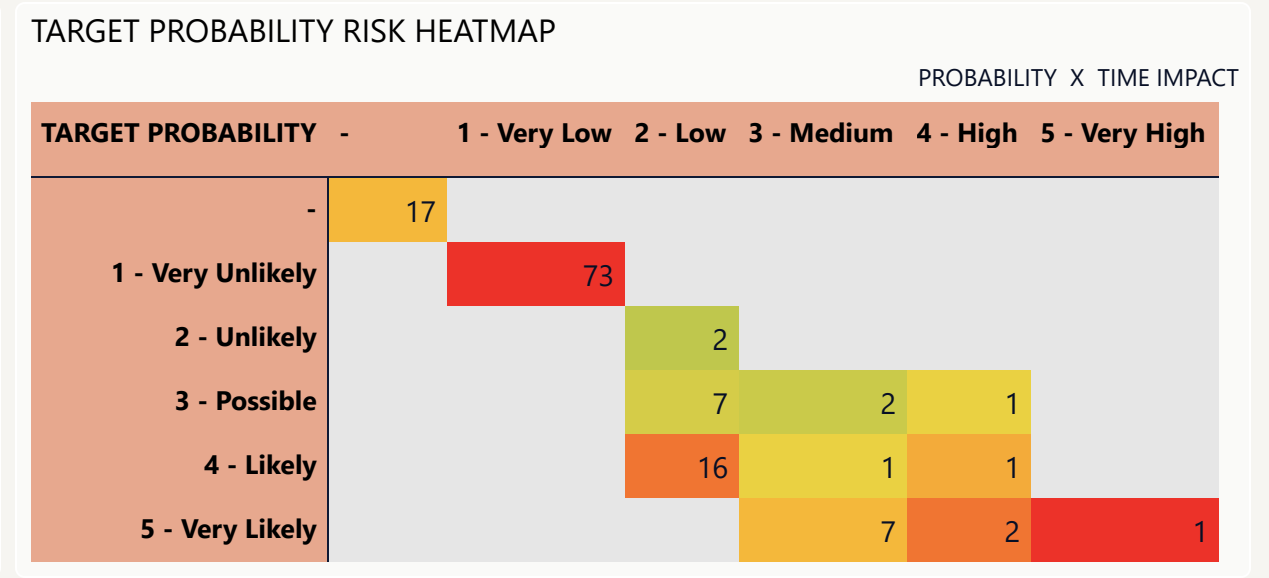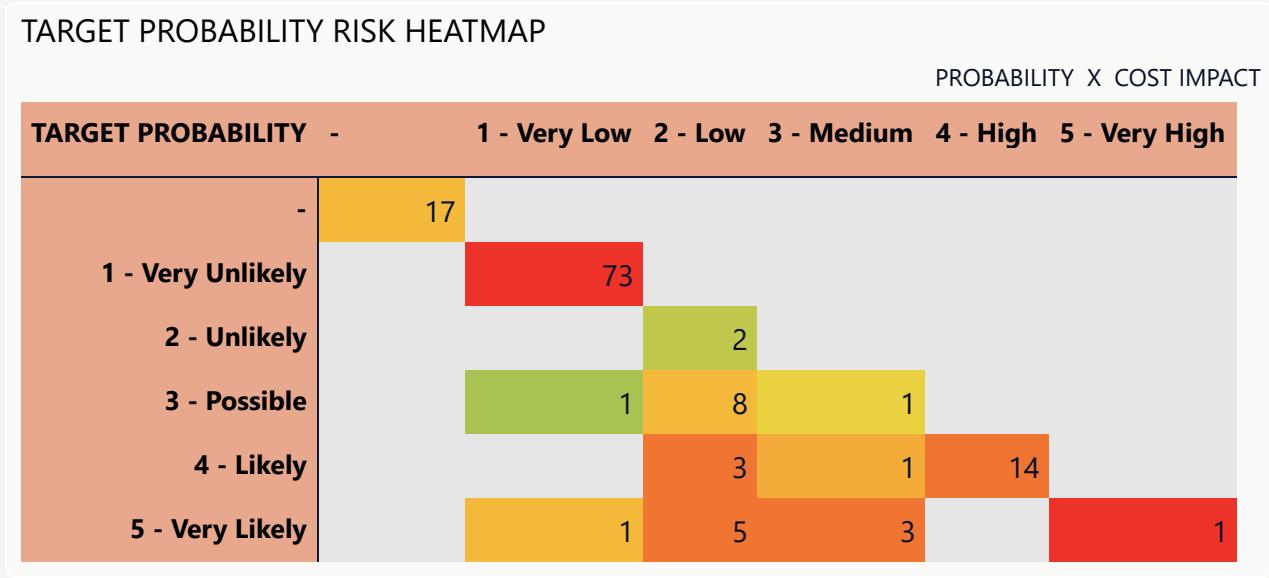



Executive Overview

Risk Exposure

Heatmap

Treatment Tracker

Milestone Impact

Risk Deep Drive

Risk Details

REDUCED

93

RESOLVED

11

ACCEPTED

8

DC VALIDATION

11

COMPLETION %

100%

OVERDUE ACTIONS

100

TREATMENT REGISTER

RISK ID	RESPONSE / MITIGATION	ACTION OWNER	STRATEGY	VALIDATION	AGING
RTH85	1. Expedite conclusion of the parking strategy for the Show Block. 2. Bulk excavation to proceed and to be progressed based on conservative excavation levels. 3. Appoint MDDC for the Show Block assets (Mixed Use Residential and Show Annex). The sameZTDesign and Development team involved in the Show House are working on other Show Block assets which will improve coordination. Done	Hesham Qadan (Item one and three) / Chris Davis (Item two)	Reduce	✗ Not Validated	611
RTH842	1. Develop and implement a Comprehensive Logistics and Access Management Plan. (The plan is not comprehensive and need improvement)	David Thomas & Nathan	Reduce	✗ Not Validated	135
RTH84	1. Expedite conclusion of the parking strategy for the Show Block as a whole. This does not effect the Show House directly as design is complete and no additional parking is required in the Show House basement. 2. Bulk excavation to proceed based on conservative excavation levels.	Hesham Qadan	Reduce	✗ Not Validated	611
RTH833	1.ZTDesign is working on proposed sketches with creative team than present to Chiefs with the implications for direction. 2. Currently under review and further design information to be assembled before next steps agreed.	Hesham Qadan		✗ Not Validated	141
RTH832	1. Matter has been raised with UMA to reach agreement for the design gap to be addressed by MUR MDDC.	Leo Solomon & Hesham Qadan		✗ Not Validated	141
RTH83	1. Detailed program and analysis to be developed based on completed 100% DD in order to ascertain substantiated construction duration - Done	Not Defined	Reduce	✗ Not Validated	611
RTH825	1. DTB sessions to be scheduled to achive design to budget. 2. All Consultants to be advised to provide more VE ideas.	Naji Syriani & Santosh Chainani		✗ Not Validated	193
RTH824	1. Utilizing the process of PS to commence work on structure. 2. Services provided won't be delayed, need further assessment. 3. Accelerate the DD redesign and fully incorporate SEC comments through a time-bound close-out plan.	Brigitta Katai-Toth Mostafa Orabi	Resolve	✗ Not Validated	165
RTH821	1. Maintain ongoing engagement withZTDelivery and UMA. 2. Expedite UMA's Task Order issuance process through early escalation and tracking.	David Thomas & Mark Ham		✗ Not Validated	165
RTH820	1. Expediate the procurement process and obtain TEC approval.	David Thomas & Mark Ham		✗ Not Validated	165
RTH82	1. Progressive update of the BIM model. 2. BIM Coordination meetings. 3. Alignment between DC, LDC and Zamil on BIM clash detection parameters to improve BIM reporting.	Hesham Qadan / Emmanuel Makhele	Reduce	✗ Not Validated	611



MILESTONE IMPACT OVERVIEW

RISK INTELLIGENCE

RISK ID

All

PROJECT

All

STATUS

All


- Executive Overview
- Risk Exposure
- Heatmap
- Treatment Tracker
- Milestone Impact
- Risk Deep Drive
- Risk Details

MILESTONES AFFECTED
11


AVG. RISK/MILESTONE
11.00

HIGHEST RISK MILESTONE
MS01 - Vision & Brief Approval (Rating: 20)

RISK BY DEVELOPMENT STAGE / MILESTONE

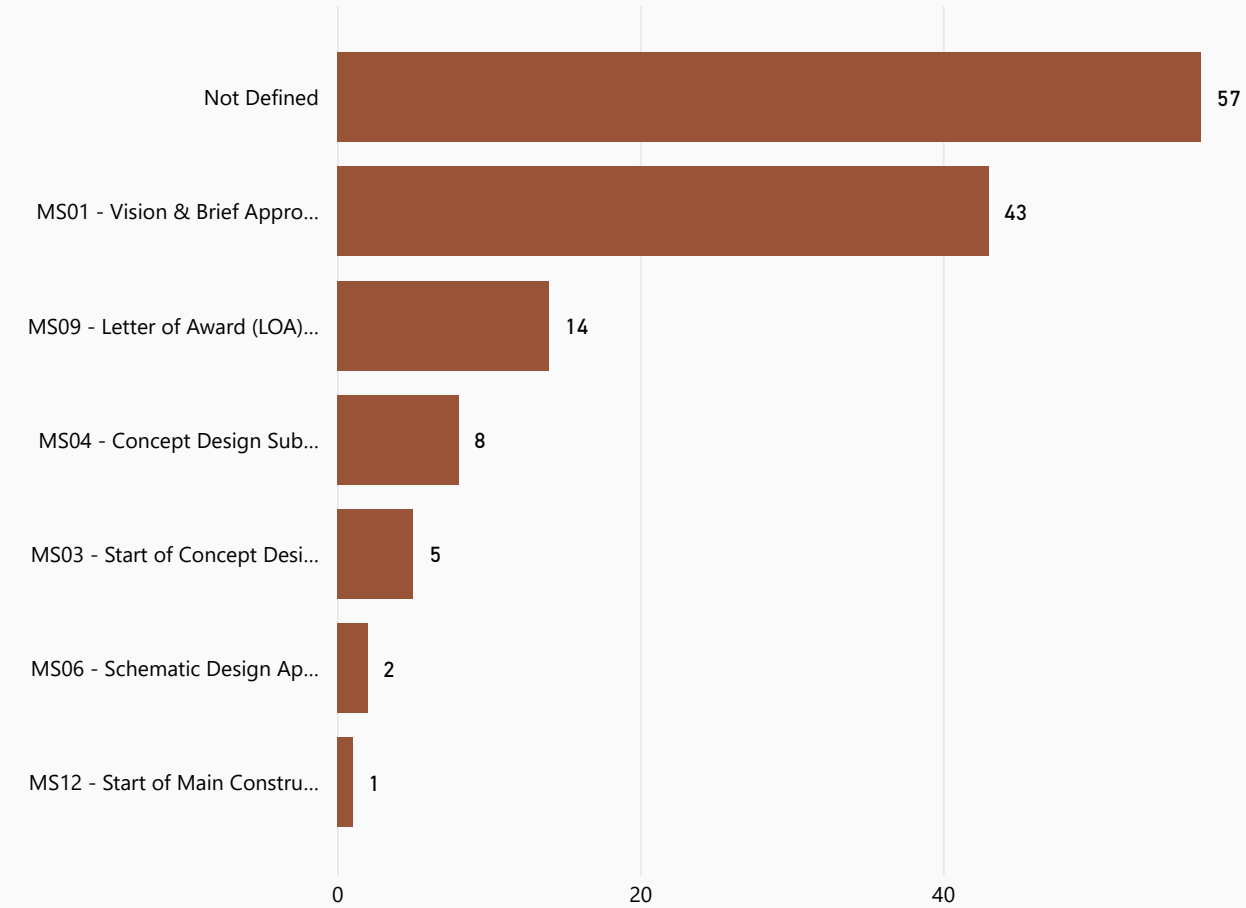

STAGE RISK SCORE

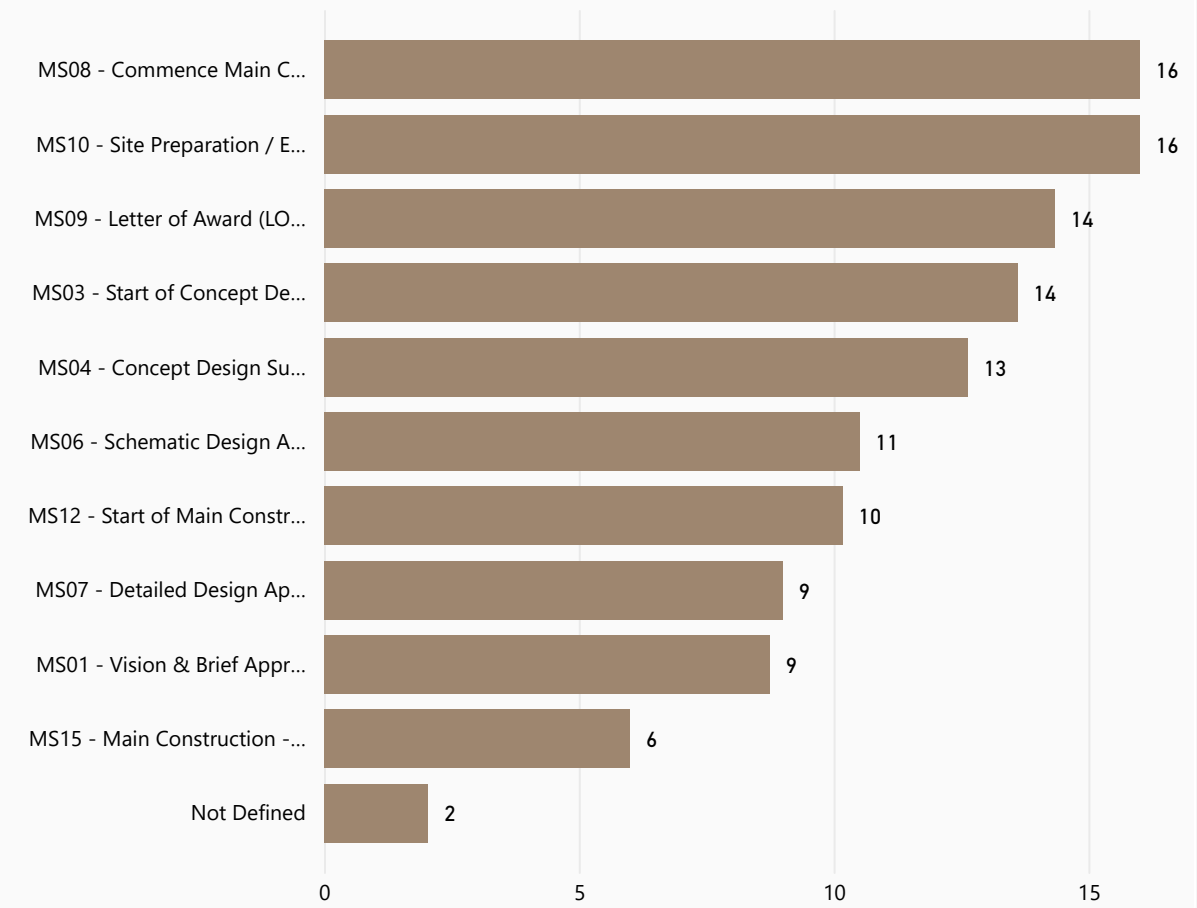



RISK DEEP-DRIVE ANALYSIS

RISK INTELLIGENCE

RISK ID
All

PROJECT
All

STATUS
All

Executive Overview

Risk Exposure

Heatmap

Treatment Tracker

Milestone Impact

Risk Deep Drive

Risk Details

RISK REGISTER - DEEP DRIVE

RISK ID	TITLE/STATEMENT	PROJECT	STATUS	INHERENT	TARGET	OWNER	AGING	TYPE	LATEST UPDATE
RTH85	Potential design conflicts and integration challenges with the other Show block assets building basement parking could arise due to inadequate coordination among design teams potentially leading to delays.	Royal AlSaja Show House	Closed	12	1	Leo Solomon	611	Threat	Risk Review workshop update [18 June 25] Risk Agreed to Close: Reason, Risk agreed to Close. Mitigation actions have been taken. Risk Review workshop update [15 May 25] 1. Show Block parking strategy progressed. Basement Parking of Mix used residential building coordinated with Show House Basement. Closed 2. Bulk excavation works near completion across the whole of Show Block. Closed.
RTH842	Risk of disruption and schedule delay due to restricted logistics flow, causing late material/equipment deliveries and reduced productivity.	Langham Hotel	Not Defined	20	20	Not Defined	135	Threat	Risk Review workshop update [21 Oct 25] new risk added
RTH84	Undetermined parking strategy / design may delay bulk excavation, affecting the project schedule.	Royal AlSaja Show House	Closed	12	1	Leo Solomon	611	Threat	Risk Review workshop update [18 Feb 25] Risk agreed to Close as Mitigated, Reason: Show House Detail Design is completed and Langham Hotel MUR is at SD stage and Parking strategy is established.
RTH833		Show Mixed-Use Assets	Open	16	16	Not Defined	141	Threat	Risk Review workshop update [15 Oct 25] Currently under review and further design information to be assembled before next steps agreed.
RTH832		Show Mixed-Use Assets	Open	16	16	Not Defined	141	Threat	Risk Review workshop update [15 Oct 25] Matter has been raised with UMA to reach agreement for the design gap to be addressed by MUR MDDC.
RTH83	Challenging schedule durations in the tender program may lead to unrealistic time planning and may reduce the contractor ability to meet the project schedule	Royal AlSaja Show House	Closed	12	1	Leo Solomon	611	Threat	Not Defined
RTH825		AlSaja Residences	Open	0	0	Not Defined	193	Threat	Risk Review workshop update [21 Oct 25] Branded resi is still DTB ongoing
RTH824	Changes in Electrical MV equipment due to comments provided by SEC will result DD redesign and delays in	Langham Hotel	Closed	15	0	Not Defined	165	Issue	Risk Review workshop update [21 Oct 25] Potential changes to design, CCF in process. Closed are we have received a letter from SEC (15-02-2025) No SEC Comment



RTH171

Internal rejection of Pre-Concept design and unsuccessful Predesign Competition



Issue

Closed

Low

DC Validated

PROJECT AlSaja Hotel	RISK SCORE 10 Inherent → 1 Target 90% Reduction %	TREATMENT Strategy : Reduce Action Owner : Vesna Ristanovic Planned Finish : Vesna Ristanovic Progress : Completed
DISTRICT TBI		
MILESTONE Not Defined	RISK STATEMENT Internal rejection of the Pre-Concept design and unsuccessful Predesign Competition may lead to design delays.	CAUSE(S) 1) Initial Pre-Concept design fails to meet internal project objectives, brand standards, or stakeholder expectations. 2) Unsuccessful outcome in the Predesign Competition 3) Location and Program Changes
DATE IDENTIFIED 04-07-2024		
RISK OWNER David Thomas	CONSEQUENCES Delays in starting Concept Design development and submission for Board of Directors (BOD) approval	MITIGATION / RESPONSE 1. Obtain the approval of Pre-Concept design.
AGEING 609 Days		
SEVERITY Very Low Risk	LATEST UPDATE Risk Review workshop update [14 Aug 24] Risk Agreed to Close: Reason, Pre-Concept design approved.	
